MYRIAD360
Rethink IT



VDI Replacement Architecture and Design

Prepared for Sysco | Myriad360 Professional Services

EXECUTIVE SUMMARY

Modernizing Sysco's Virtual Desktop Infrastructure

Myriad360 will deliver a comprehensive assessment, architecture, detailed design, and proof-of-concept deployment to enable Sysco's evaluation and selection of a next-generation VDI platform — replacing the existing Omnissa Horizon environment.

What We're Delivering

A full six-stage engagement spanning assessment of the current environment, new target-state architecture development, detailed design documentation, and remote POC deployment across 5 workload cohorts.

Primary Scope

2 physical data centers · up to 10 servers · ~40,000 compute users · up to 500 applications · 5 POC workload cohorts across Windows 365, AVD, Island, and Citrix DaaS.

Intended Outcome

Sysco will receive a validated, decision-ready architecture and POC results to support an informed, evidence-based platform selection and production roadmap.

Delivery Approach

A structured, phased engagement combining onsite discovery and working sessions with remote architecture review, design, and POC deployment — managed by a dedicated Myriad360 Project Manager.

ENGAGEMENT OVERVIEW

Six-Stage Engagement at a Glance

01

Stage 1 — Assessment

Onsite assessment of the existing Omnissa Horizon environment across 2 data centers and up to 10 physical servers.

02

Stage 2 — Assessment Review

Onsite structured review session with Sysco stakeholders to present Stage 1 findings and align on next steps.

03

Stage 3 — Architecture Development

Target-state VDI platform architecture developed using a portfolio approach across Windows 365, AVD, Island, and Citrix DaaS.

04

Stage 4 — Architecture Review

Remote architecture review session with Sysco stakeholders and one revision cycle based on feedback.

05

Stage 5 — Detailed Design

Comprehensive Detailed Design Document covering all 5 POC workload cohorts across all approved platforms.

06

Stage 6 — POC Deployment

Remote deployment assistance for up to 5 workload cohorts within Sysco's existing Azure tenant.

IN SCOPE

Stage 1 — Current Environment Assessment *(Onsite)*

Myriad360 will conduct an onsite assessment of the existing Omnissa Horizon VDI environment. All activities will be performed during mutually agreed-upon maintenance windows and business hours.

Infrastructure & Topology

- VDI infrastructure topology, persistent and non-persistent pool configurations, and session-host specifications across up to **10 physical servers**
- Profile architecture, storage dependencies (including Isilon), and FSLogix or App Volumes configuration
- Network topology, regional connectivity architecture, and round-trip latency baselines for: **United States, Europe, India, and the Philippines**
- Infrastructure cost baselines, current licensing model, and Omnissa renewal and hardware end-of-life dates

Applications & User Personas

- Application inventory covering up to **500 thick applications** and up to **100 entitlement groups**, including legacy dependencies (ODBC, OCX, DLL)
- User persona and job-family groupings representing approximately **40,000 compute users**, based on Sysco-provided data

Telemetry & Performance Data

- Available telemetry from **Omnissa Intelligence, Nextthink, and Intune** for usage, concurrency, logon duration, and application launch data

Identity & Access

- Entra ID, Conditional Access, MFA, App Volumes, and domain configuration

Security Stack

- Forcepoint, Netskope, Zscaler, SentinelOne, Nessus, and Tanium integrations
- Applicable SOC 2 and GDPR control documentation as provided by Sysco security and compliance owners

Assessment Report Output

Myriad360 will produce a written **Assessment Report** documenting: current-state environment, identified data gaps, technical risks, open platform-selection decisions, and a findings summary across infrastructure, application, persona, security, and performance domains.

IN SCOPE

Stage 2 — Assessment Review & Stage 3 — Architecture Development

Stage 2 — Assessment Review (Onsite)

- 1 onsite structured review session with Sysco stakeholders presenting Stage 1 Assessment Report findings
- Agenda covers: current-state environment summary, data gaps, technical risks, persona and application findings, security and compliance observations, and recommended next steps
- Myriad360 will capture stakeholder feedback and publish a written **Session Summary** within 5 business days of the session

Stage 3 — Architecture Development (Onsite)

- Target-state VDI platform architecture developed using a portfolio approach covering: **Windows 365, Azure Virtual Desktop, Island, and Citrix DaaS**
- 1 onsite working session with Sysco technical and architecture stakeholders to validate design decisions and resolve dependency conflicts across identity, network, security, profile, and application delivery

Architecture Output Includes:

- Recommended service catalog: secure browser access, managed cloud PC (persistent), pooled desktop (non-persistent), published application delivery, specialized workstation, and exception/legacy service tiers
- Platform-to-persona mapping aligned to the 5 POC workload cohorts
- Regional deployment design for the United States and at least 1 additional confirmed target region (Europe, India, or the Philippines)
- Identity, security, and compliance integration requirements per service catalog tier
- POC environment design within Sysco's Azure tenant, including virtual network topology, identity integration approach, and platform-specific resource requirements

IN SCOPE

Stage 4 — Architecture Review & Stage 5 — Detailed Design

Stage 4 — Architecture Review (Remote)

- 1 remote review session with Sysco stakeholders to present the proposed target-state architecture from Stage 3
- Stakeholder feedback captured during or within 5 business days following the session
- Up to **1 revision cycle** incorporated based on feedback
- Written **Architecture Review Summary** published documenting all decisions made, outstanding open items, and the approved direction for detailed design

Stage 5 — Detailed Design Document (DDD)

A comprehensive Detailed Design Document covering all **5 POC workload cohorts** and all approved platforms. The DDD includes:

- Architecture overview narrative and approved service catalog definitions
- Platform-specific configuration requirements for Windows 365, AVD, Island, and Citrix DaaS
- Identity and access design: Entra ID, Conditional Access, MFA, and hybrid identity architecture
- Network design: regional connectivity, Azure virtual network topology, subnet allocation, and security group definitions within Sysco's Azure tenant
- Security stack integration requirements for each service tier (Forcepoint, Netskope, Zscaler, SentinelOne, Tanium)
- Profile and data management design: FSLogix configuration specifications and OneDrive integration guidance
- Per-workload POC deployment specifications for each of the 5 cohorts
- Visio diagrams: logical architecture, physical architecture, network topology, identity flow, and service tier relationships

Up to **1 revision cycle** incorporated based on customer feedback received within 5 business days of initial delivery.

IN SCOPE

Stage 6 — POC Deployment Assistance *(Remote)*

Myriad360 will provide remote deployment assistance for a Proof of Concept covering **up to 5 workload cohorts** within Sysco's existing Azure tenant.

Browser-First Contractor

Island-based browser delivery of SaaS and Microsoft 365 from managed or unmanaged endpoints

Call-Center Worker

Windows 365 persistent Cloud PC with standard application stack, voice, and media capability

Finance User

Windows 365 or AVD configured for large-profile workloads, spreadsheet applications, and licensed financial applications

Global Knowledge Worker

Windows 365 or AVD tested from at least 1 high-latency region (India, Philippines, or Europe as confirmed at kickoff)

Legacy Application User

AVD or Citrix DaaS configured for applications with ODBC, OCX, or DLL dependencies as identified in Stage 1

For each workload cohort, Myriad360 will configure the applicable platform, validate against mutually approved success criteria, and document results in a **per-workload POC Results Report**. A consolidated **POC Summary Report** will be produced at the conclusion of Stage 6 covering outcomes across all 5 workloads, platform scorecard results, and recommended next steps.

POC activities are limited to 1 provisioning and configuration cycle per workload. Changes to workload scope, platform selection, or success criteria after configuration has begun require a mutually approved change order.

OUT OF SCOPE

What Is Not Included in This Engagement

Migration & Production Deployment

- Production migration of any users, applications, workloads, profiles, or data from Omnissa Horizon to any target platform
- Full platform deployment of Windows 365, AVD, Island, or Citrix DaaS beyond the 5 defined POC workloads
- Wave migration planning, migration execution, or cutover management
- Decommissioning of existing Omnissa Horizon infrastructure, servers, or related components

Application Services

- Application troubleshooting, remediation, repackaging, sequencing, or dependency resolution for legacy applications
- Custom scripting, automation development, or tooling creation beyond standard platform configuration
- Custom application development of any kind

Infrastructure & Physical Work

- Hardware procurement, sourcing, or vendor coordination of any kind
- Rack and stack services at any data center or facility
- Structured cabling or physical network installation
- Assessment of infrastructure, servers, applications, or systems outside the Omnissa Horizon environment

Security & Compliance

- Creation, modification, or formal approval of security policies, Conditional Access policies, DLP policies, or compliance frameworks

Vendor & Procurement

- Third-party vendor remediation or coordination (Citrix, Microsoft, Island, Netskope, Zscaler, SentinelOne, Nessus, Tanium)
- Vendor RFP preparation, scoring, or procurement support
- Platform licensing procurement or negotiation on behalf of the customer
- Three-year TCO financial modeling or business case development

Operations & Support

- Managed services or ongoing operational support following project completion
- End-user training or training material development of any kind
- After-hours or weekend work unless mutually agreed upon in writing prior to the applicable activity

POC Scope Boundary

- POC workloads beyond the 5 cohorts explicitly identified in this Statement of Work

ASSUMPTIONS

Engagement Assumptions — Access & Prerequisites

The following assumptions establish important conditions and customer responsibilities that must be met for this engagement to proceed as scoped.

Environment Access — Stage 1

Sysco will provide Myriad360 with read and appropriate administrative access to the **Omnissa Horizon environment, Omnissa Intelligence, Nextthink, and Intune** prior to the start of Stage 1 activities.

Technical Documentation

Sysco will provide all required network diagrams, IP addressing information, credentials, configuration documentation, and technical documentation prior to the start of each applicable project stage.

Azure Tenant Access — Stage 6

Sysco will provide authorized access to Sysco's Azure tenant with sufficient permissions (**Contributor-level or equivalent**) for Myriad360 to configure and deploy POC resources during Stage 6.

Platform Licensing — Stage 6

Sysco is responsible for the procurement, activation, and readiness of all platform trial or production licenses required for POC workloads (**Windows 365, AVD, Island, Citrix DaaS**) prior to the start of Stage 6 activities.

Telemetry Availability

Telemetry data from Omnissa Intelligence, Nextthink, and Intune will be made available prior to Stage 1. If data is unavailable or incomplete, assessment conclusions for affected areas will be explicitly qualified and documented as data gaps within the Assessment Report.

Azure Subscription Costs

Azure subscription costs and platform licensing costs incurred during POC deployment within Sysco's Azure tenant are the **sole responsibility of Sysco**.

ASSUMPTIONS

Engagement Assumptions — Stakeholders, Scheduling & Onsite Requirements

Stakeholder Availability

Sysco will make required technical stakeholders available for each onsite session during Stages 1, 2, and 3. Required stakeholder groups include: **VDI and endpoint operations, identity and directory services, network engineering, security and compliance, and application ownership**.

Onsite Location Scope

Onsite activities for Stages 1, 2, and 3 will be performed at up to **2 physical data center locations within the contiguous United States**. Additional locations identified after project kickoff are outside the scope of this engagement.

Facility Access

Sysco will provide Myriad360 personnel with physical facility access, guest network connectivity, and required building entry credentials for all onsite activities at each data center location prior to each scheduled visit.

Maintenance Windows

Sysco will confirm mutually agreed-upon maintenance windows for any assessment activities requiring access to production systems. Myriad360 will not access production systems outside of approved maintenance windows.

Named Project Coordinator

Sysco will designate a **named project coordinator** who is authorized to approve deliverables, provide or coordinate system access, and make scheduling decisions on behalf of Sysco for the duration of the engagement.

POC Test Users

Sysco will identify and make available a minimum of **1 representative test user per POC workload cohort** prior to the start of Stage 6.

ASSUMPTIONS

Engagement Assumptions — Timeline, Reviews & Change Control

1 POC Success Criteria

POC success criteria — including logon time thresholds, application launch time targets, session reliability requirements, and security control validation criteria — will be defined and mutually approved in writing during project kickoff, prior to the start of Stage 6.

2 Engagement Duration

The engagement is scoped for a duration of up to **3 calendar months** from the date of project kickoff. Schedule delays caused by customer unavailability, incomplete prerequisites, or access delays do not extend the engagement timeline without a mutually approved change order.

3 Deliverable Review & Approval

Sysco will provide written review and approval of all deliverables within **5 business days of submission**. Delays beyond 5 business days may impact the project schedule and are not the responsibility of Myriad360.

4 Scope Boundary — Change Orders

Additional devices, servers, data center locations, users, applications, or POC workloads beyond the quantities identified in this Statement of Work require a **mutually approved change order**. Sysco is responsible for procurement, receipt, licensing, and readiness of all customer-provided hardware and software prior to implementation activities.

DELIVERABLES

Formal Project Deliverables

The following formal deliverables will be produced and submitted to Sysco for review and written approval as part of this engagement.

1

High-Level Design (HLD)

Target-state VDI platform architecture including service catalog, platform-to-persona mapping, regional deployment design, identity and security integration requirements, and POC environment design.

2

Project Plan

Integrated project plan covering the full engagement timeline, milestone schedule, resource assignments, and tracking cadence maintained throughout the engagement by the Myriad360 Project Manager.

3

Low-Level Design (LLD)

Detailed Design Document (DDD) covering all 5 POC workload cohorts: platform-specific configurations, identity and access design, network design, security stack integrations, profile management, and Visio architecture diagrams.

4

Validation Report

Consolidated POC Summary Report documenting outcomes across all 5 workloads, per-workload pass/fail results against defined success criteria, identified defects, and platform scorecard with recommended next steps for production evaluation.

5


Project Closure Acceptance

Formal project closure documentation confirming completion of all in-scope activities, deliverable acceptance, and open item disposition.

PROJECT TIMELINE

Phased Project Approach

This engagement is structured across 6 sequential stages designed to build upon each other, from discovery through validated proof of concept. The engagement is scoped for a duration of **up to 3 calendar months** from the date of project kickoff.

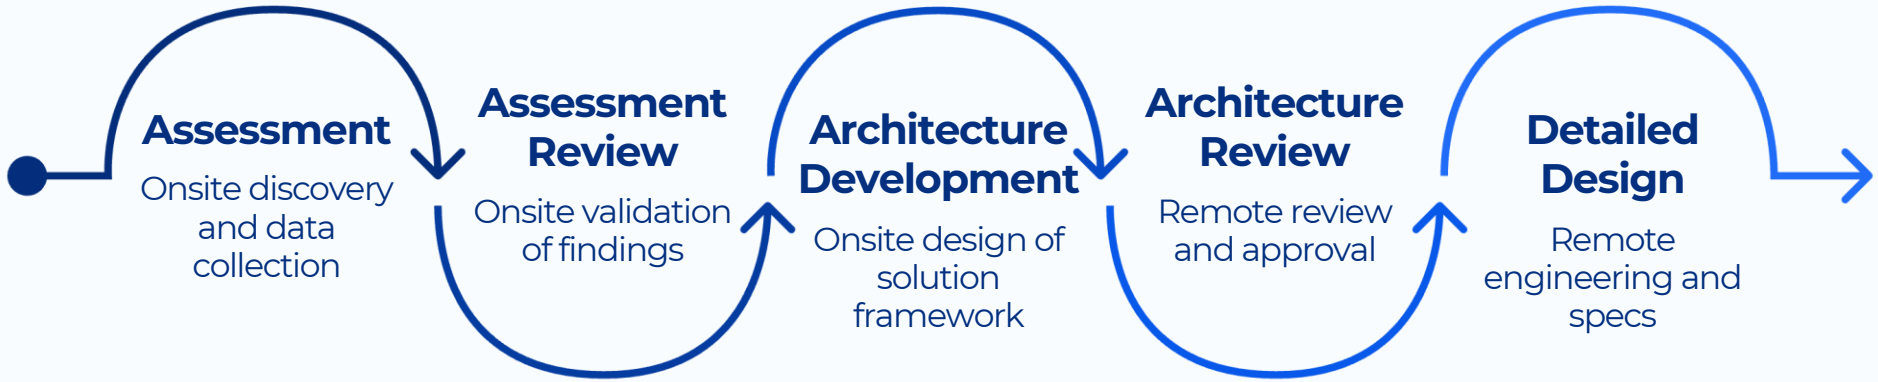

Onsite Phases (Stages 1–3)

- **Stage 1:** Current environment assessment across 2 data centers
- **Stage 2:** Assessment review session with Sysco stakeholders
- **Stage 3:** Architecture development working session

Remote Phases (Stages 4–6)

- **Stage 4:** Remote architecture review and revision cycle
- **Stage 5:** Detailed design documentation with revision cycle
- **Stage 6:** POC deployment across 5 workload cohorts

PROJECT MANAGEMENT

Your Dedicated Partner in Project Success

Our Project Managers are the driving force behind every successful engagement. They ensure seamless coordination, proactive communication, and complete accountability from project kickoff to closeout.

End-to-End Ownership

From initiation through closure, PMs oversee schedule, resources, and budget across the full engagement lifecycle.

Expert Coordination

Alignment of internal teams, vendors, and partners for smooth execution across all project phases.

Accountability

Ownership of outcomes, client satisfaction, and continuous improvement throughout the engagement.

Quality & Consistency

Standardized tools and processes for visibility and control at every stage.

Global Delivery

Coordination of complex and distributed environments spanning multiple regions and teams.

PROJECT MANAGEMENT

What You Can Expect

Our Promise

Reliable execution, clear accountability, and consistent delivery from kickoff through closeout.

Project management for this engagement is scoped for the full duration — **up to 3 calendar months** from the date of project kickoff — and includes kickoff facilitation, weekly written status reporting, issue and risk log maintenance, and a formal project closure summary.

Your Single Point of Contact Will Provide:

- **Single point of contact** for all project communication and coordination
- **Clear communication** with regular written status updates
- **Proactive issue management** and escalation when required
- **Budget tracking** and change control throughout the engagement
- **Integrated project plan** and reporting from kickoff to closure

INVESTMENT

Engagement Investment Summary

This engagement is offered as a **fixed-fee investment**, providing Sysco with cost certainty across all six stages of the VDI Replacement Architecture and Design engagement.

Engagement	Fixed-Fee Investment
VDI Replacement Architecture and Design Full six-stage engagement including assessment, architecture, detailed design, and POC deployment for Sysco	**$88,778**

Fixed-Fee Terms

The investment above is a fixed fee. All six stages and all formal deliverables are included within this investment as scoped in this Statement of Work.

What's Included

Onsite assessment (2 data centers), assessment review, architecture development and review, detailed design documentation, POC deployment assistance (5 workloads), and project management.

Customer Responsibilities

Azure subscription costs and platform licensing costs incurred within Sysco's Azure tenant during POC activities are the sole financial responsibility of Sysco and are not included in this investment.

Additional scope, locations, servers, applications, or POC workloads beyond those identified in this Statement of Work require a mutually approved change order and may result in additional investment.

MYRIAD360
Rethink IT

Next Steps

We look forward to partnering with Sysco on this engagement. The following actions will set the project in motion.

1

Review & Accept

Review this Service Brief and the associated Statement of Work. Confirm alignment on scope, assumptions, and investment.

2

Execute Agreement

Sign the Statement of Work to authorize the engagement and formally initiate the project.

3

Schedule Kickoff

Coordinate with your Myriad360 Project Manager to schedule the project kickoff session and confirm Stage 1 onsite dates.

4

Prepare Prerequisites

Begin coordinating access, stakeholder availability, technical documentation, and facility requirements in advance of Stage 1 activities.
